



S.R. 202, Section 61S
East Norriton Township, Montgomery County



Construction Update November 2024

On SR202 between Carriage Lane and Hartranft Boulevard, the contractor completed the installation of the new sanitary sewer system, service lateral tie-ins and the abandonment of the old system between Johnson Highway and Hartranft Boulevard. The contractor also completed drainage installation and began roadway excavation and grading.



Once roadway grading is complete, the contractor plans to place stone subbase and bituminous pavement between Johnson Highway and Hartranft Boulevard.

On SR202 between Hartranft Boulevard and Germantown Pike, the contractor completed the construction of erosion and control sedimentation basins on the southbound side of SR202, at Lawnton Road and near Colonial Drive. The contractor also installed protective waterproof membrane on the culvert at Jefferson Crossing and installed temporary traffic signal equipment at multiple intersections.






Construction Update November 2024

This fall, the contractor will begin installation of the temporary drainage and construction of the sedimentation basin on the northbound side of the SR202, near Germantown Pike. This will be followed by the excavation and placement of temporary pavement widening between Chick-Fil-A and Germantown Pike. After the temporary pavement widening is completed, the contractor intends to traffic shift into the long-term Stage 1 traffic pattern and begin drainage installation on the southbound side of the roadway.

On SR202 between Germantown Pike and Township Line Road, the contractor completed the installation of the new drainage system on Dekalb Boulevard and began the excavation for the new noise barrier wall between Dekalb Pike and Dekalb Boulevard.

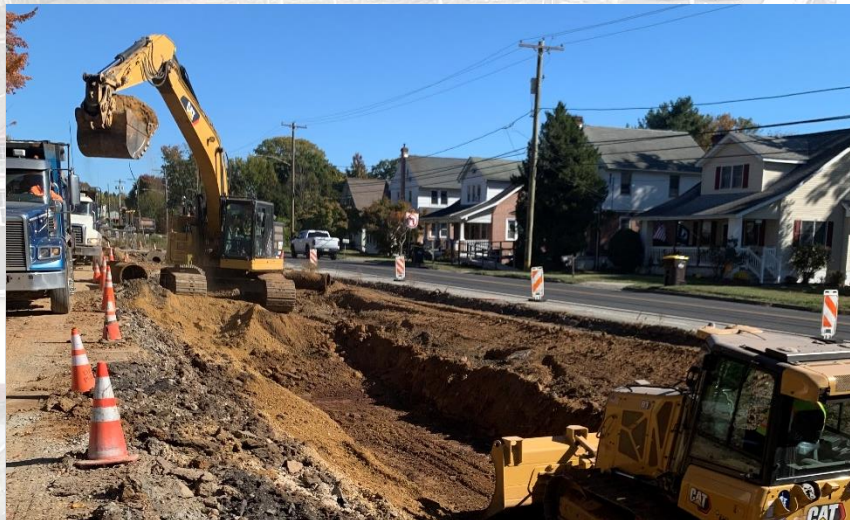

This fall, the contractor will continue with the excavation for the new noise wall, followed by the construction of the cast-in-place concrete foundation slab and stem wall. Following construction of the noise wall, the contractor will begin the installation of the new drainage on the SR202 side of the wall. The contractor will also begin the installation of the new sanitary sewer system between Germantown Pike and McDonalds.

On Township Line Road, the PECO Gas contractor began the installation of the new 12" steel gas main and the relocation of service connections, on the east side of SR202, near Butchers Lane.



S.R. 202, Section 61S
East Norriton Township, Montgomery County
Construction Update
November 2024



This fall, PECO Gas will continue with their main installation on the east side of SR202, followed by the relocation and lowering of gas main in the middle of the SR202 and Township Line Road intersection. PECO Gas will then install a new main on Township Line Road between Swede Road and DeKalb Pike. PECO Electric's contractor will install new underground cables on the north side of Township Line Road between Swede Road and DeKalb Pike. Installation of the new sanitary sewer system will begin after the relocation of the underground electric and PECO Gas main.

The SR202-61S project is scheduled to be completed by the end of 2027.
