

Stage 1 - 30th to SAW - A & B Stages for Utility Work on Bridge & CSX Advanced Substructure - end March 2025 to mid March 2026

No Road Work/Lane Closures - start of June 2026 - middle of of Aug 2026 for 250th Anniversary

Stage 2 - River Bridge (14 Month Detour - start of August 2026 to mid October 2027); includes ABC Intersection replacement During Stage 2A/2B - (October 2026, March 2027-August 2027); 2A/2B - advanced substructure (caissons) for CSX

Stage 3 - CSX - A (mid October 2027 to start of May 2028) & B (start of May 2028 to end of October 2028)

Stage 4 - Final Clean Up (Entire Project) - end of October 2028 - end of February 2029

Pre-stage PECO Utility Work (not in MSB contract) - Planned Prior to Nov 2024

Stage W0 - Short Term Off-Peak Temp PPBL & Signals from 30th Street to 24th Street. (end of March 2025 to mid July 2025)

Stage W1 - Short Term Off-Peak - Joint Replacement (mid July 2025 to start of February 2027, stops during 250th anniversary closure);


No Road Work/Lane Closures - start of June 2026 - middle of Aug 2026 for 250th Anniversary

Stage W2 - Short Term Off-Peak - Milling & Scarification - start of February 2027 to start of April 2027

Stage W3 - Accelerated Latex Modified Concrete Overlay on 4 Weekends (April 2027 to May 2027)

Stage W4 - Construct Barrier Curb Traffic Separators - end of May 2027 - end of August 2027

Utility & Roadway Reconstruction performed Stages 2 & 3

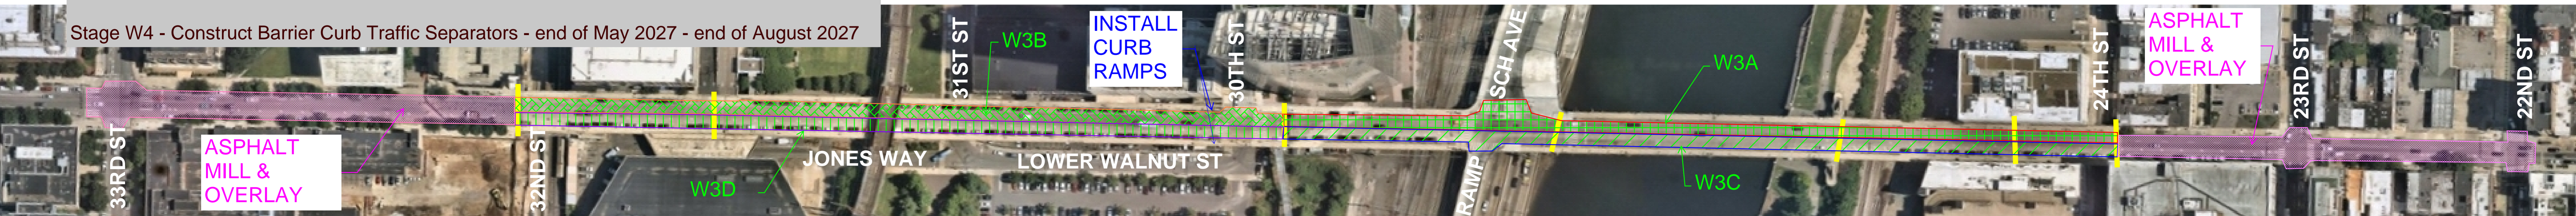

INSTALL CURB RAMPS

ASPHALT MILL & OVERLAY

ASPHALT MILL & OVERLAY
