

TRAFFIC CONTROL PLAN

DISTRICT	COUNTY	TOWNSHIP	BOROUGH	ROUTE	SECTION	TOTAL SHEETS
4-0	SUSQUEHANNA	GIBSON	----	2046	570	2

ECMS NO. 112539

GENERAL NOTES FOR MAINTENANCE AND PROTECTION OF TRAFFIC

THIS WORK CONSISTS OF THE MAINTENANCE OF TRAFFIC AND THE PROTECTION OF THE TRAVELING PUBLIC APPROACHING THE CONSTRUCTION AREA AND WITHIN THE LIMITS OF CONSTRUCTION.

FURNISH, ERECT, PLACE AND MAINTAIN TRAFFIC CONTROL SIGNS AND DEVICES AND MAINTAIN TRAFFIC DURING HOURS OF CONSTRUCTION AND AT ALL OTHER TIMES IN ACCORDANCE WITH THE METHODS INDICATED ON THESE DRAWINGS, AND:

1. THE SPECIAL PROVISIONS OF THE CONTRACT.
2. FEDERAL HIGHWAY ADMINISTRATION, MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES MUTCD).
3. PUBLICATION 213, TEMPORARY WORK ZONE TRAFFIC CONTROL GUIDELINES.
4. PUBLICATION 212, OFFICIAL TRAFFIC CONTROL DEVICES.
5. PUBLICATION 35, QUALIFIED PRODUCTS LIST FOR CONSTRUCTION (BULLETIN 15).
6. PUBLICATION 408, SPECIFICATIONS.
7. PUBLICATION 236, HANDBOOK OF APPROVED SIGNS.
8. PUBLICATION 46, TRAFFIC ENGINEERING MANUAL.

THE CONTRACTOR IS TO NOTIFY LOCAL EMERGENCY UNITS (POLICE, FIRE, MEDICAL, ETC.), LOCAL BUSINESSES, PENNDOT PERMITS UNIT, LOCAL SCHOOL DISTRICTS, LOCAL MEDIA, PENNDOT ICC AT 570-963-4058 AND PENNDOT DISTRICT 4-0 C.R.C. AT 570-963-4044 TWO (2) WEEKS AND ALSO TWENTY FOUR (24) HOURS PRIOR TO THE START OF WORK OR AT THE START OF A NEW CONSTRUCTION PHASE AND WHEN ROAD IS OPEN TO UNRESTRICTED TRAFFIC.

CONTRACTOR IS TO PROVIDE NOTIFICATION TO THE INSPECTOR-IN-CHARGE OF THE FOLLOWING:

- START OF PHYSICAL WORK -- SEVEN CALENDAR DAYS
- WIDTH, HEIGHT, OR WEIGHT RESTRICTIONS TO ANY ROADWAY -- TEN WORKING DAYS (EXCLUDING STATE HOLIDAYS) NOTE: RESTRICTIONS ARE FROM THE PRE-CONSTRUCTION WIDTH, HEIGHT, OR WEIGHT RESTRICTION.
- REMOVAL OF WIDTH, HEIGHT, OR WEIGHT RESTRICTIONS TO ANY ROADWAY -- IMMEDIATELY UPON REMOVAL
- START OF ANY OPERATION AFFECTING TRAFFIC (LANE CLOSURES, TOTAL CLOSURES, ETC.) -- SEVEN CALENDAR DAYS WITH A CONFIRMATION THE MORNING THE OPERATION BEGINS.

ALL SIGNS TO BE MOUNTED ON TYPE III BARRICADES UNLESS OTHERWISE NOTED.

COORDINATE WORK ZONE SIGNING AND OPERATIONS WITH PROJECTS IN THE AREA.

ALL TRAFFIC CONTROL DEVICES SHALL BE NEW OR LIKE NEW CONDITION AND MAINTAINED AS SUCH.

REFER TO ITEM NO. 0901-0001 - MAINTENANCE AND PROTECTION OF TRAFFIC DURING CONSTRUCTION, WITHIN THE PROJECT CONTRACT FOR ADDITIONAL INFORMATION PERTAINING TO THIS PROJECT.


REFER TO THE CONSTRUCTION REQUIREMENTS, CONSTRUCTION RESTRICTIONS, AND HOLIDAY RESTRICTIONS, WITHIN THE PROJECT CONTRACT FOR ADDITIONAL INFORMATION PERTAINING TO THIS PROJECT.

REFER TO PUBLICATION 213, TEMPORARY WORK ZONE TRAFFIC CONTROL GUIDELINES, GENERAL NOTES SECTIONS (A) THROUGH (I) FOR ADDITIONAL INFORMATION.

TABULATION OF TRAFFIC CONTROL DEVICES


(FOR INFORMATION ONLY)
INCLUDED IN ITEM 0901-0001

STD. NO.	SIZE (IN)	DESCRIPTION	QUANTITY
D 3-1	VAR X 12	STREET NAME SIGN - "FIDDLE LAKE ROAD"	17
M4-10L	48 X 18	DETOUR ARROW, LEFT	1
M4-8A	24 X 18	END DETOUR	2
M4-9L	30 X 24	DETOUR, LEFT	2
M4-9R	30 X 24	DETOUR, RIGHT	4
M4-9S	30 X 24	DETOUR, STRAIGHT	5
M4-9SL	30 X 24	LEFT ADVANCE DETOUR	2
M4-9SR	30 X 24	RIGHT ADVANCE DETOUR	2
R11-2	48 X 30	ROAD CLOSED	2
R11-3A	60 X 30	ROAD CLOSED - LOCAL TRAFFIC ONLY	2
W20-2	36 X 36	ADVANCE DETOUR	4
W23-101	96 X 48	THIS ROAD TO BE CLOSED FOR MAINTENANCE	2
W30-1-2	20 X 6	DISTANCE (1000 FT) (PANEL)	1
W30-1-3	20 X 6	DISTANCE (1500 FT) (PANEL)	1
W30-1-6	20 X 6	DISTANCE (AHEAD) (PANEL)	2
		TYPE B LIGHT (AMBER)	SUFF.
		TYPE III BARRICADE	SUFF.

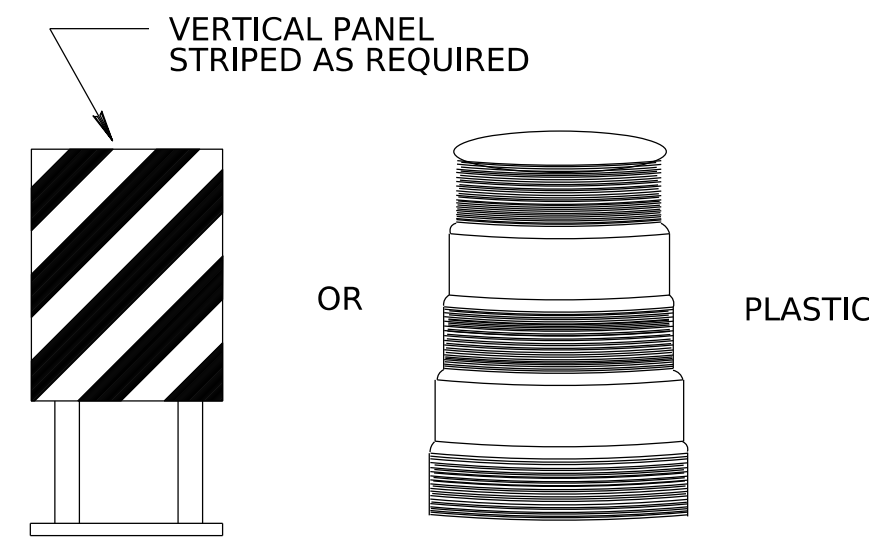

CHANNELIZING DEVICE DETAIL

NOT TO SCALE



RECOMMENDED _____ 20 _____

DISTRICT TRAFFIC ENGINEER



TRAFFIC CONTROL PLAN

DETOUR PLAN - SR 2046 SEG 0012

ROAD CLOSED - DETOUR LENGTH 6.3 MILES

DISTRICT	COUNTY	ROUTE	SECTION	SHEET
4-0	SUSQUEHANNA	2046	570	2 OF 2
GIBSON TOWNSHIP				
REV NO	REVISIONS	DATE	BY	APPD

OPERATOR: egraebner
FILE NAME: pw://PDEDPRAPPW01.penn.dot.lcl:Connect_Projects/Documents/OpenRoads_Projects/D04/57 - Susquehanna/57 2046 570 (112539) Bridge Rehab/Roadway/Rusthil Pate/Traffic Plan - 57-2046
16-JUL-2024 14:28
PLOTTED:

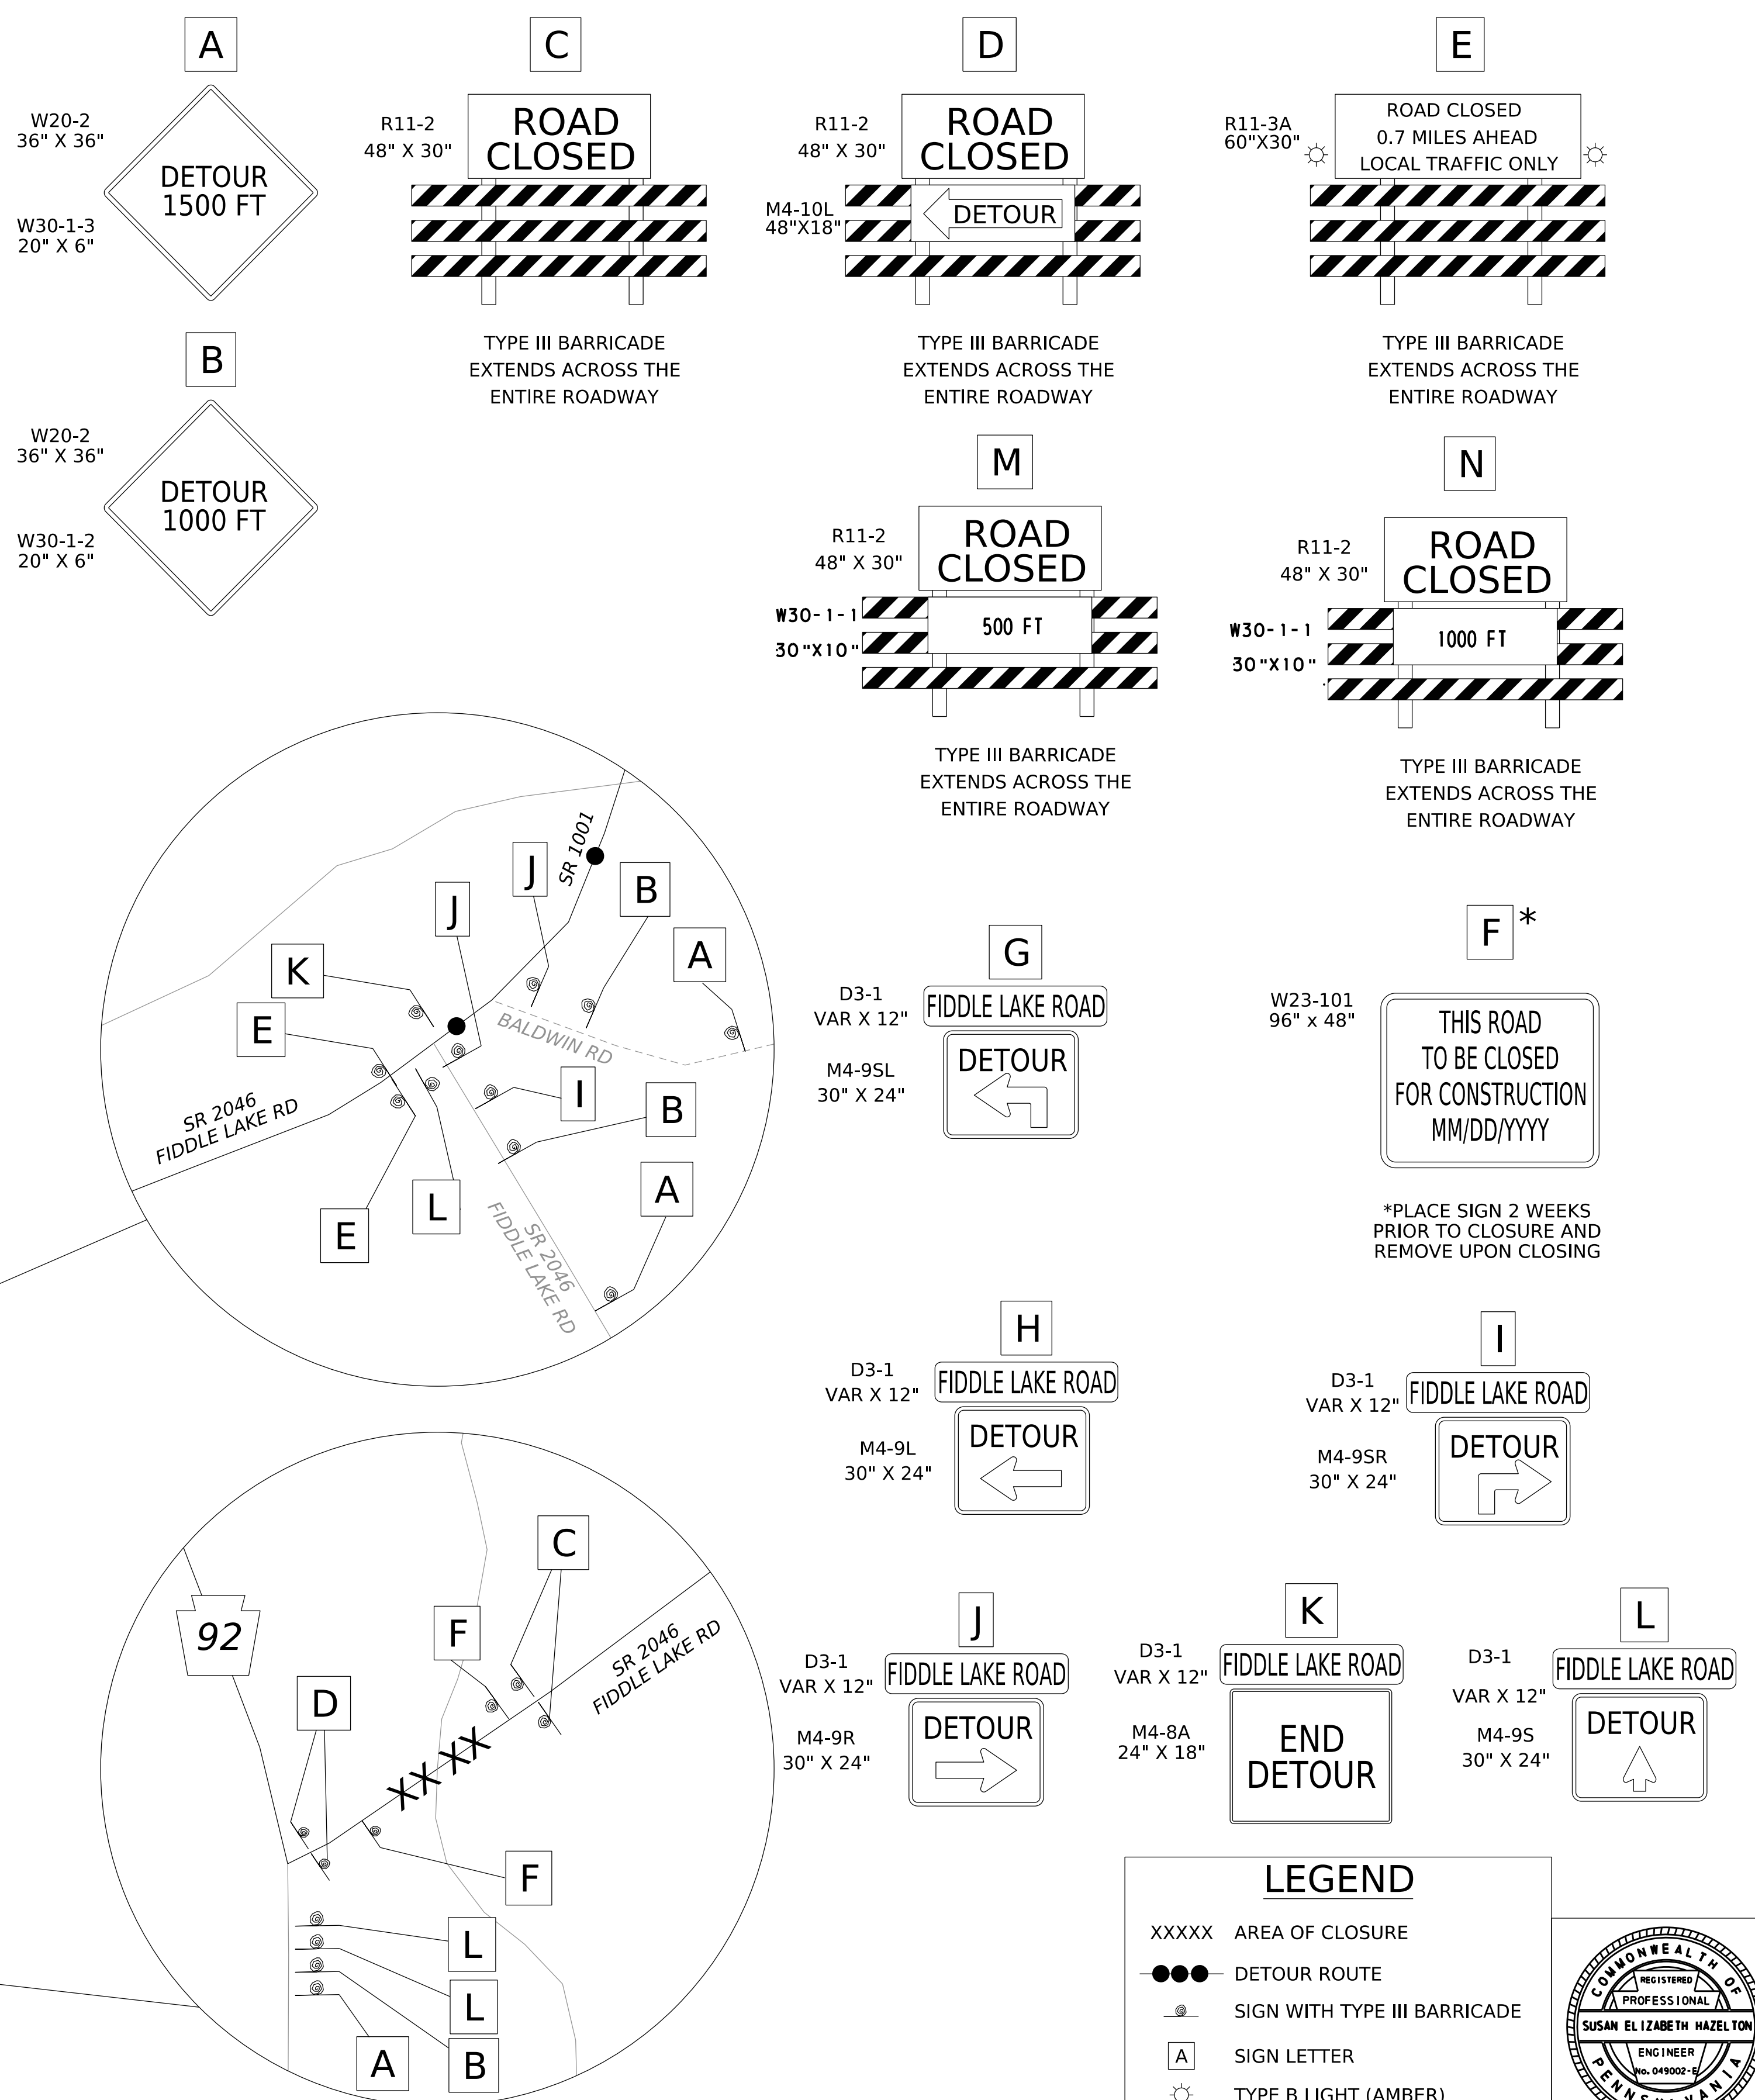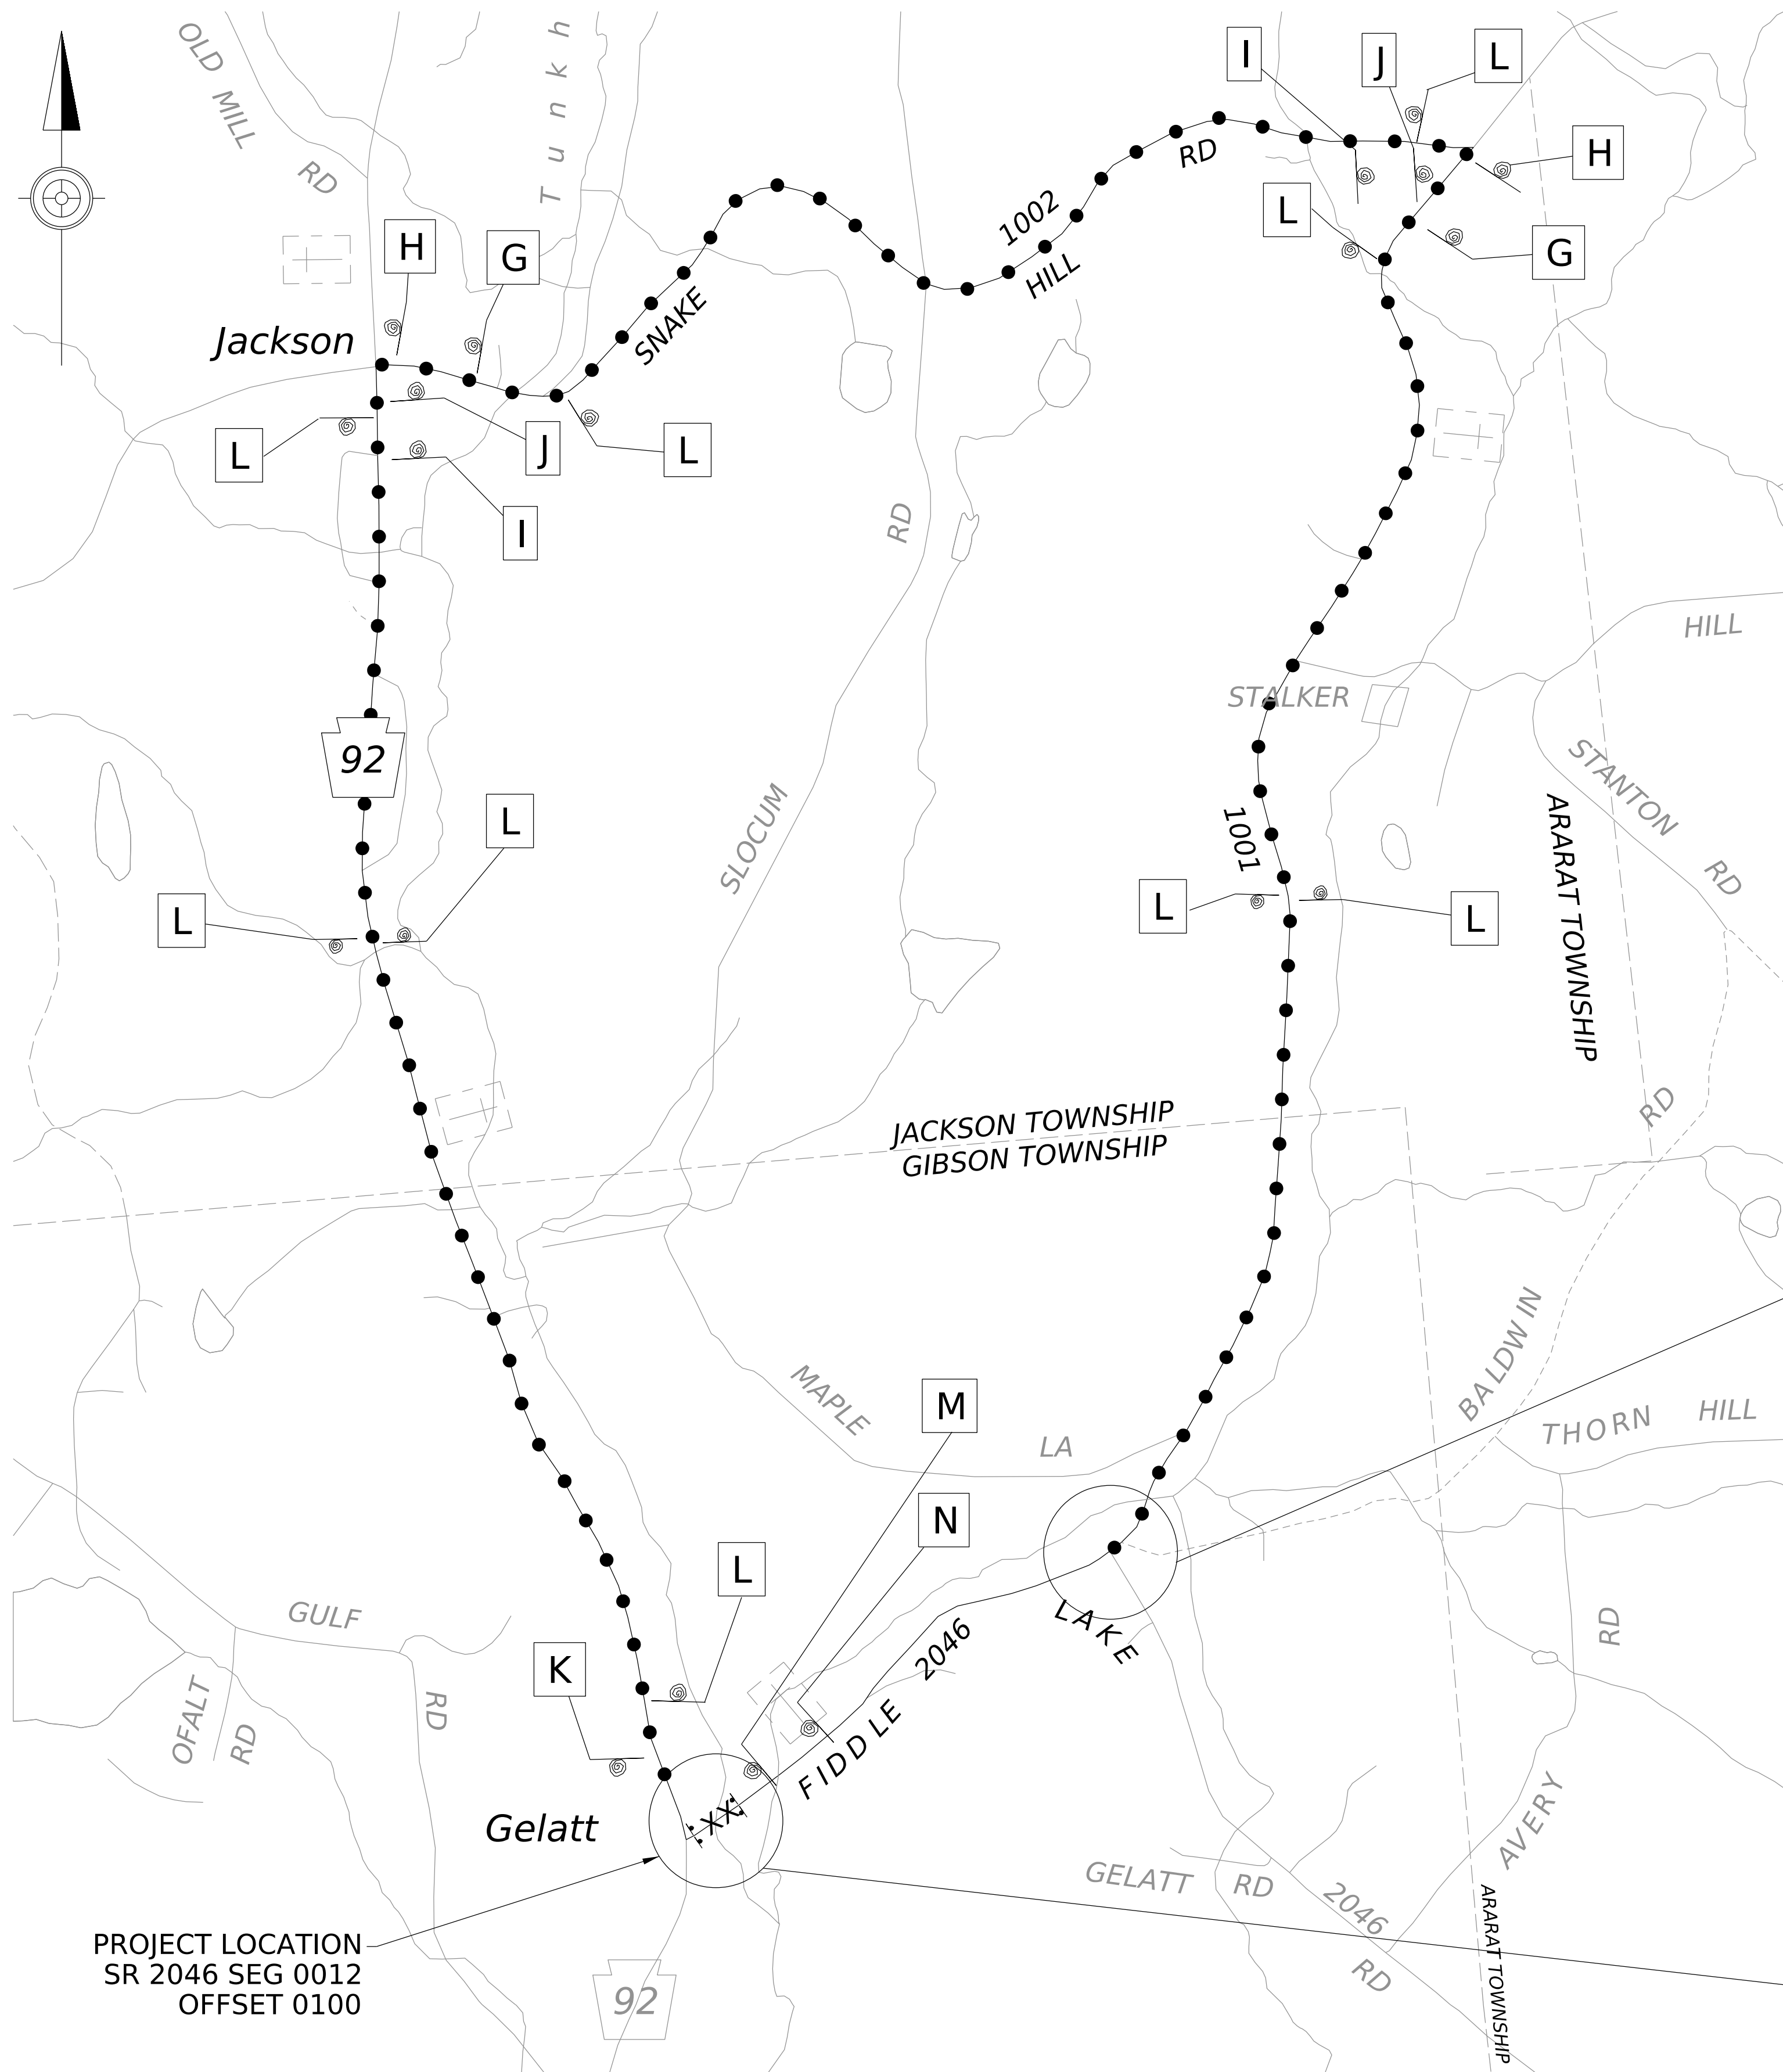

NOT TO SCALE

